

Cabinet

A meeting of the Cabinet will be held on:

Date: Tuesday, 8 June 2010

Time: 3.00pm

Venue: Meeting Room 2 - Level 3, Gun Wharf, Dock Road, Chatham ME4 4TR

Membership:	Councillor Rodney Chambers	Leader of the Council
	Councillor Alan Jarrett	Portfolio Holder for Finance and Deputy Leader
	Councillor Janice Bamber	Portfolio Holder for Customer First and Corporate Services
	Councillor Jane Chitty	Portfolio Holder for Strategic Development and Economic Growth
	Councillor Howard Doe	Portfolio Holder for Housing and Community Services
	Councillor Phil Filmer	Portfolio Holder for Front Line Services
	Councillor Tom Mason	Portfolio Holder for Adult Services
	Councillor Mike O'Brien	Portfolio Holder for Community Safety and Enforcement
	Councillor Les Wicks	Portfolio Holder for Children's Services
	Councillor David Wildey	Portfolio Holder for Children's Social Care

Agenda


11. Gateway 3 Contract Award: A228 Stoke Crossing

**(Pages
1 - 2)**

Revised Risk Register tabled at the meeting.

For further information please contact Wayne Hemingway/Anthony Law, Cabinet Coordinators on Telephone: 01634 332509/332008 or Email: democratic.services@medway.gov.uk

Date: 8 June 2010

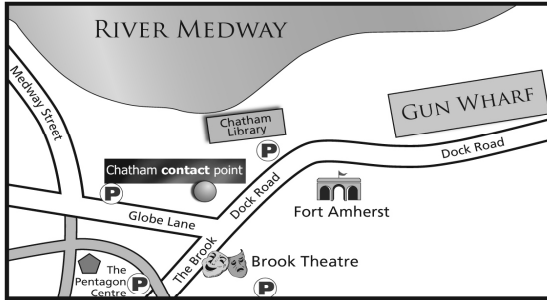

This agenda and reports are available on our website
www.medway.gov.uk

A summary of this information can be made available in other formats from **01634 333333**

If you have any questions about this meeting and you want to speak to someone in your own language please ring **01634 335577**

উালা	331780	गुजराती	331782	ਪੰਜਾਬੀ	331784	كوردی	331841	اروو	331785	Русский	332374
中文	331781	हिंदी	331783	Polski	332373	এইহুশাফব	331786	فارسی	331840	Lietuviškai	332372

RISK REGISTER - A228 Stoke Crossing

D= Avoid, A = Accept, R = Reduce, T = Transfer

No.	Item	Details	Initial Probability VH/H/M/L	Initial Consequence VH/H/M/L	DART Classification	Method of Control	Residual Probability VH/H/M/L	Residual Consequence VH/H/M/L
1	Funding	Failure to obtain contributions would detrimentally affect project viability	M	VH	R	Negotiations with National Grid Property are in progress. A formal agreement will depend on NR submitting an acceptable planning application.Planning consent granted and S106 in place	0	Discharged
2	Environmental Problems	Problems in gaining approval of Natural England or onerous pre-commencement planning conditions	H	H	R	Early consultation has involved Natural England, RSPB and EA. Environmental impact has been anticipated at outline design stage. All parties are being kept fully briefed on the issues and there is an ongoing dialogue	L	VH
3	HCA Funding	Construction would be in 2010/11 and HCA has not guaranteed funding for year 3	H	VH	R	Continue dialogue with HCA to explain progress. HCA have been fully involved in the negotiations with National Grid Funding is currently agreed, is signed off and as of 8 June 2010 is in place.	M	VH
4	Ground Conditions	Poor ground conditions lead to increased costs	H	L	T	It is known from the location that the ground conditions will be very poor and this has been factored into the estimates. Detailed site investigation completed	0	Discharged
5	Network Rail Agreement	Delay in obtaining NR permission to build over the railway could delay the project	L	H	D	NR are fully supportive of the project and are willing to make a small financial contribution. NR will be involved in design development.Design details submitted in accordance with NR requirements	L	L
6	Planning Permission	Failure to obtain planning permission would prevent project progress	L	H	R	There is local support for the principle of the scheme, objections are most likely to be on environmental grounds which is why stakeholders have been involved at project inception.	L	VH
7	Tender Values	Tender values exceeding the approved budget would impose a high risk on the Council	L	H	D	Prospective tenderers will be involved at an early stage to give a view as to the robustness of estimates.Tenders now received	0	Discharged
8	Timing	Slight delays in delivery may affect seasonal work so delaying the project by a substantial period	L	H	D	The project planning takes account of seasonal works and separate early contracts will be let for site clearance etc.The tendered scheme takes account of seasonal work	0	Discharged
9	Land	Delay or failure to acquire the necessary land would delay the project or prevent it being carried out	L	H	D	CPO powers will be sought if there is a resistance to negotiation Negotiations are well advanced, the primary remaining risk is completion	M	VH

This page is intentionally left blank
